


Works Notice Progress Update: Main Road causeway, Mt Pleasant: Replacement of damaged culverts, construction of a new seawall and road repairs

Included in this update is information about the progress made so far on the causeway repairs.

Progress made so far on the Main Road causeway works:

The countdown is on! 34 days to go. We're running on schedule for completion by 1 November 2013.

- The western and eastern culverts have been replaced.
- The seawall restoration works are now 80% complete.
- The existing main culvert has been demolished and a new bridge sits in its place.
- Kerb and channel replacement has started, along with the footpath replacement.
- Pavement reconstruction has started, with completion scheduled for mid-October.
- The section of the coastal pathway along the causeway is 20% complete.

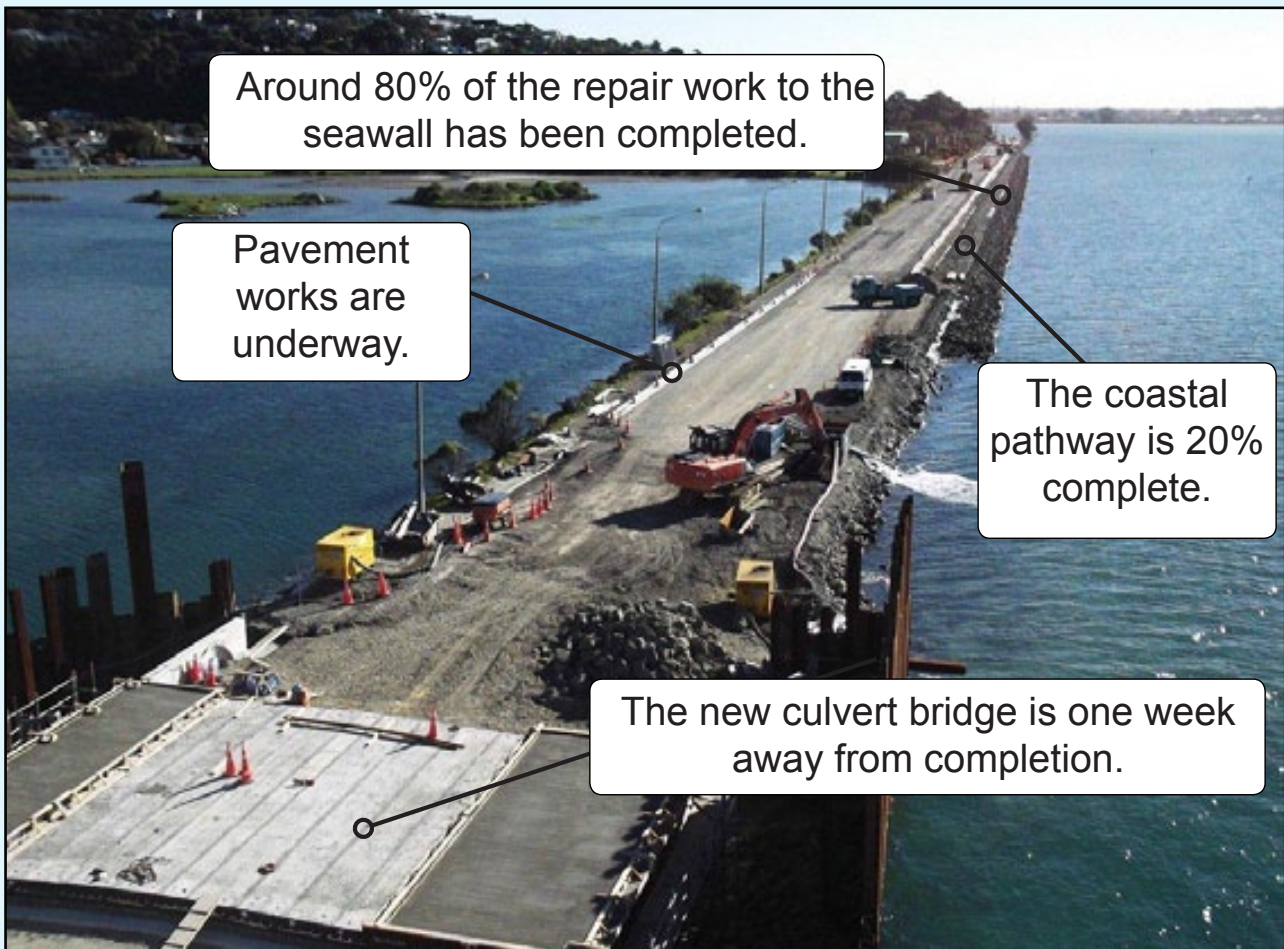

Please turn over

Photos of the culvert bridge progressing:



Bright young minds visit causeway:

Canterbury University students were given the opportunity to visit the causeway work site last month. After a safety briefing on-board, two bus loads of Civil Engineering students were escorted onto the causeway site by the Fulton Hogan crew. The causeway's Project Manager, Cherie Leckner, explained the construction of the culvert bridge structure and how the seawall was being built and answered the students questions.

The students conceptual design project this year is the long-term options for McCormacks Bay; coming on a site tour of Fulton Hogan's causeway project was a great opportunity to see up-close what is already being done by Fulton Hogan and SCIRT. The site tour was enjoyed by all involved so we would also like to give the public a chance to see our work up close.

Don't miss your chance to see the causeway up close while it is still under construction!

Fulton Hogan would like to invite the local community to an open day of the causeway work site: You can't see all of the progress from McCormacks Bay Road so come and have a closer look at the causeway's seawalls and the culvert bridge structure while they are still under construction.

Date: Sunday 6 October 2013

Time: 10:30am – 12:30pm

Location: Please park near the sports ground on McCormacks Bay Road and walk to the site entrance on the Sumner side - you will be escorted onto the site.

Please visit www.strongerchristchurch.govt.nz for more information about the Main Road causeway project.

Need more information?

Phone: 0800 277 34 34 (8.30am- 5.00pm Monday - Friday)

Email: rebuildinfo@fultonhogan.com

Website: Visit www.strongerchristchurch.govt.nz

Follow us on Twitter: twitter.com/scirt_info

34 days to go.

Keep an eye out for the countdown along McCormacks Bay Road.

Email: info@scirt.co.nz
www.strongerchristchurch.govt.nz



Visit our website and sign up to receive our e-newsletter for the latest information.
Follow us on Twitter @SCIRT_info

 **Fulton Hogan**

Christchurch City Council 

Programme funded by

New Zealand Government
